CORVANE BIOLOGICS

Q3 2026 Report to the Board of Directors

Board meeting, 22 October 2026, Visp
Presented by the Executive Committee

STRICTLY CONFIDENTIAL



Agenda

1	CEO summary	S. Zurbriggen	3
2	Organisation update	S. Volken	4
3	Financial performance Q3	M. Oggier	6
4	Revenue, backlog and cash	M. Oggier	7
5	Operations and quality	A. Kalbermatten, E. Ruppen	11
6	Risks and project portfolio	S. Zurbriggen	13
7	Outlook and decisions requested	S. Zurbriggen	18
8	Appendix		19

For decision

LY-5 lyophiliser investment, CHF 38.0 m

Extension of the revolving credit facility to CHF 120 m

For information

Q3 results and FY 2026 guidance

Quality and CAPA status

Risk register, Q3 review

Click a line to jump to the section.

CEO summary: a record quarter, with two watch points

REVENUE (CHF)

61.4 m ↑

+13.9 % vs Q3 2025

EBITDA MARGIN

27.8 % ↑

+2.6 pts vs Q3 2025

BATCHES RELEASED

212 ↑

+6 % vs Q2, FL-3 and FL-5

RIGHT FIRST TIME

97.6 % ↓

target 98.0 %

ON TIME IN FULL

94.1 % ↓

−1.8 pts: LY-2 maintenance

LTI RATE

0.42 ↑

per 200,000 h, target < 0.5

Growth

PFS demand drives revenue: FL-5 at 92 % of planned capacity, two new commercial contracts signed.

Margin

Mix and fixed-cost absorption lift EBITDA to CHF 17.1 m, CHF 1.3 m above budget.


Watch point 1

LY-2 unplanned maintenance (11 days) cost 9 batches and pushed OTIF below target.

Watch point 2

Right-first-time below target on FL-3 after the stopper supplier change; CAPA 26-118 in progress.

Organisation: Executive Committee and site leadership

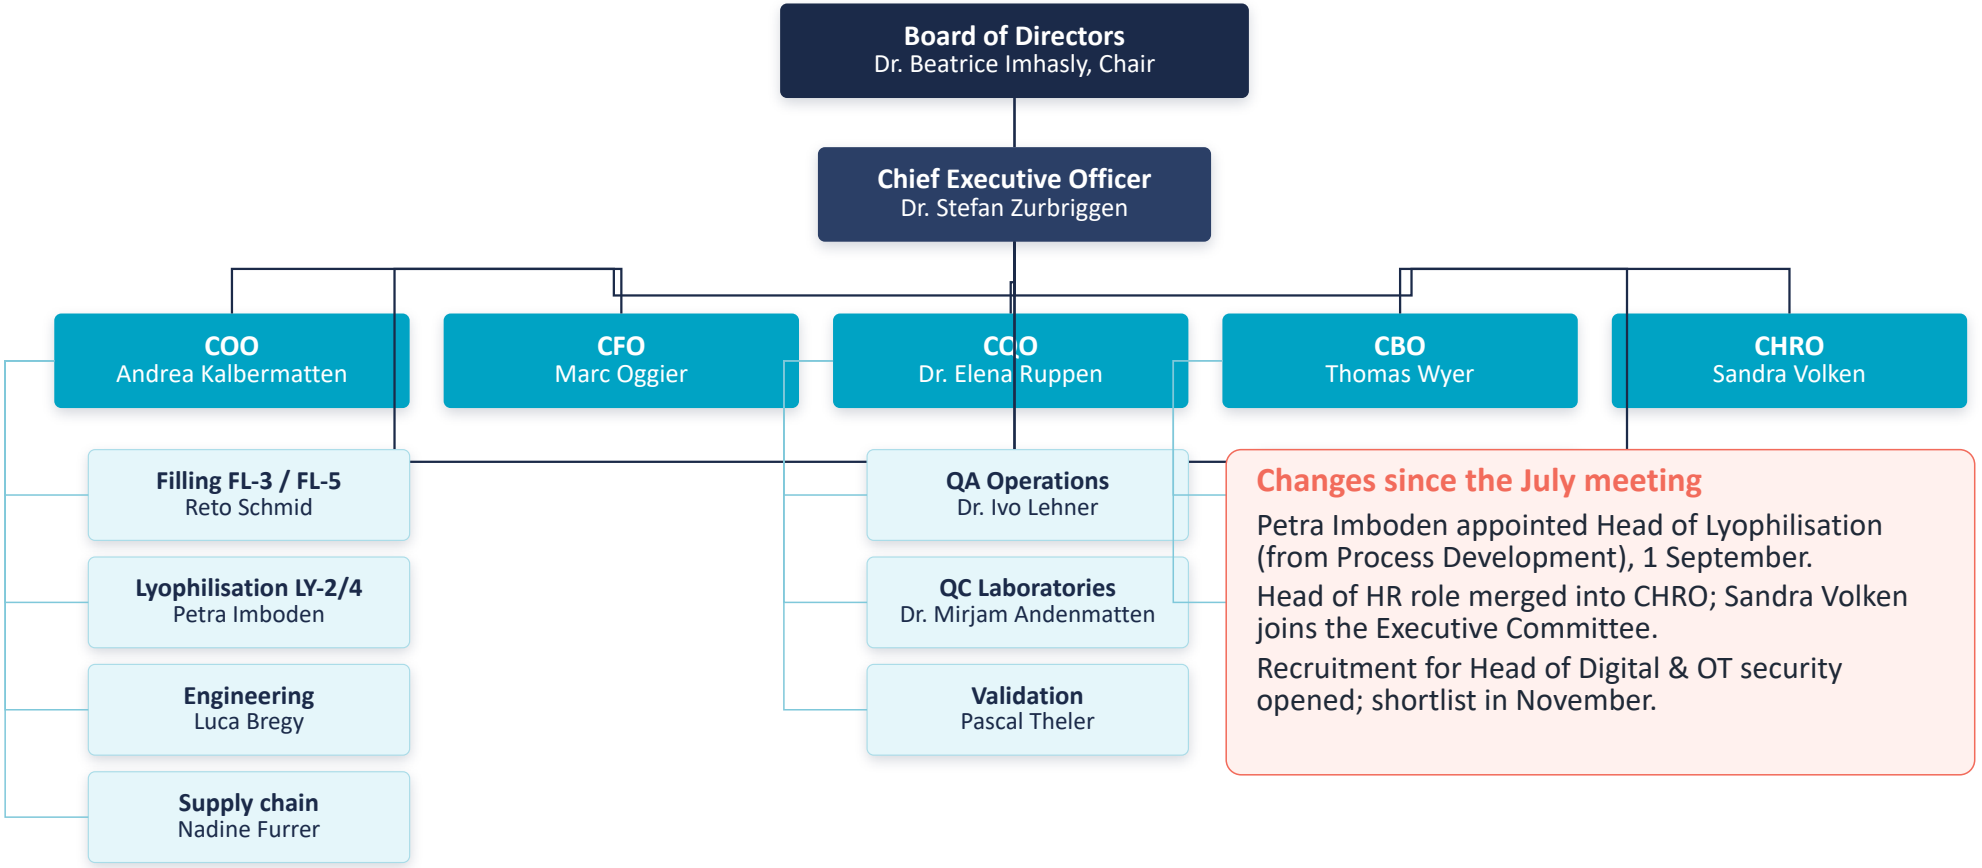

Changes since the July meeting

Petra Imboden appointed Head of Lyophilisation (from Process Development), 1 September.

Head of HR role merged into CHRO; Sandra Volken joins the Executive Committee.

Recruitment for Head of Digital & OT security opened; shortlist in November.

CORVANE BIOLOGICS

01


Financial performance

Revenue CHF 61.4 m, EBITDA CHF 17.1 m, net cash CHF 71.9 m.

Q3 2026 income statement

CHF million	Q3 2026	Q3 2025	Δ %	Budget Q3	Δ vs budget
Revenue	**61.4**	**53.9**	**+13.9 %**	**59.8**	**+1.6**
Fill-finish, vials	27.6	24.9	+10.8 %	27.1	+0.5
Prefilled syringes	16.9	13.2	+28.0 %	15.6	+1.3
Lyophilised products	11.3	10.4	+8.7 %	11.6	−0.3
Development and analytical services	5.6	5.4	+3.7 %	5.5	+0.1
Cost of goods sold (excl. D&A)	−36.2	−32.6	+11.0 %	−35.6	−0.6
Gross profit	**25.2**	**21.3**	**+18.3 %**	**24.2**	**+1.0**
Selling, general and administrative	−6.1	−5.8	+5.2 %	−6.3	+0.2
Process development	−2.0	−1.9	+5.3 %	−2.1	+0.1
EBITDA	**17.1**	**13.6**	**+25.7 %**	**15.8**	**+1.3**
EBITDA margin	27.8 %	25.2 %	+2.6 pts	26.4 %	+1.4 pts
Depreciation and amortisation	−5.9	−5.2	+13.5 %	−6.0	+0.1
EBIT	**11.2**	**8.4**	**+33.3 %**	**9.8**	**+1.4**
Net financial result and taxes	−2.2	−1.8	+22.2 %	−2.1	−0.1
Net profit	**9.0**	**6.6**	**+36.4 %**	**7.7**	**+1.3**

Revenue and EBITDA margin, last eight quarters

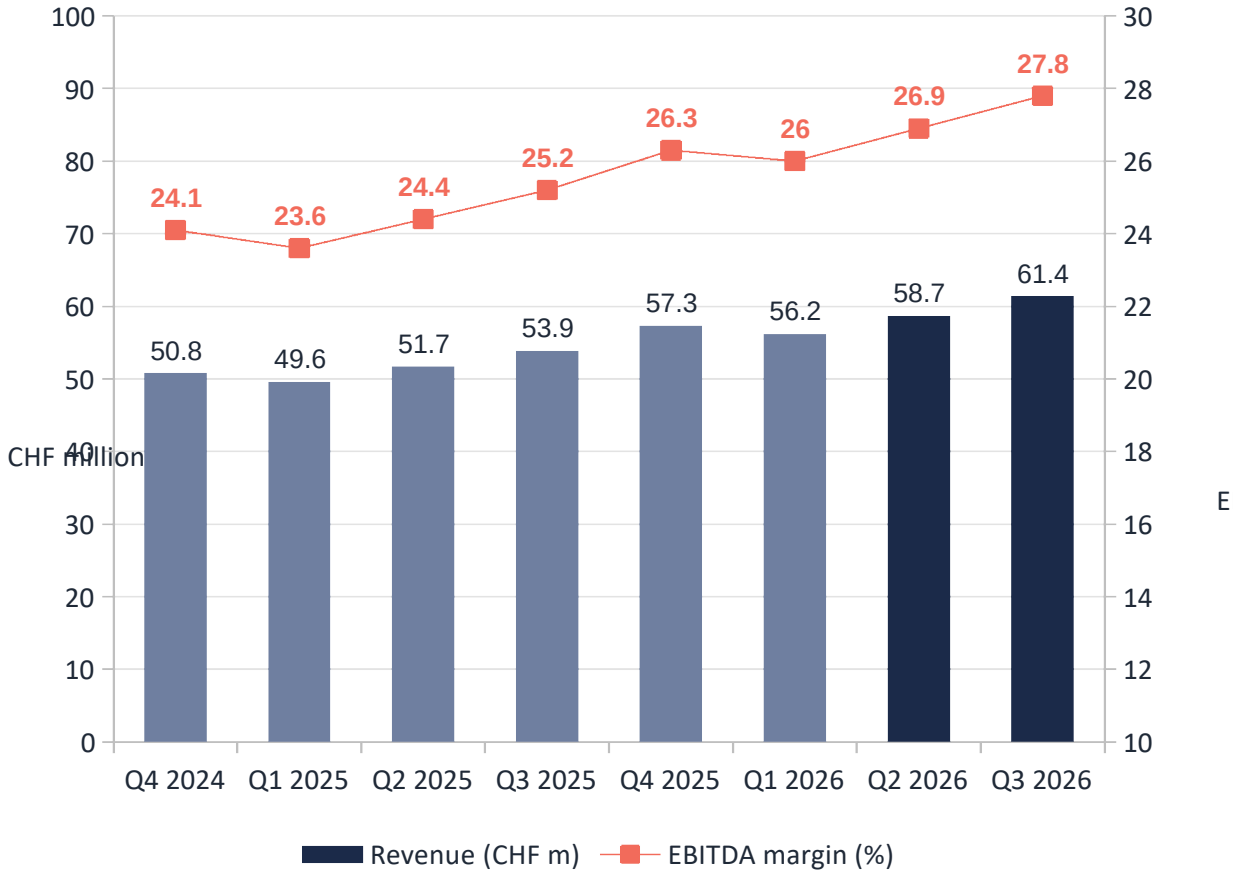

+20.9 %

revenue growth Q3 2026 vs Q4 2024


+3.7 pts


EBITDA margin over eight quarters

CHF 233.6 m

revenue, last four quarters

Order backlog and revenue mix

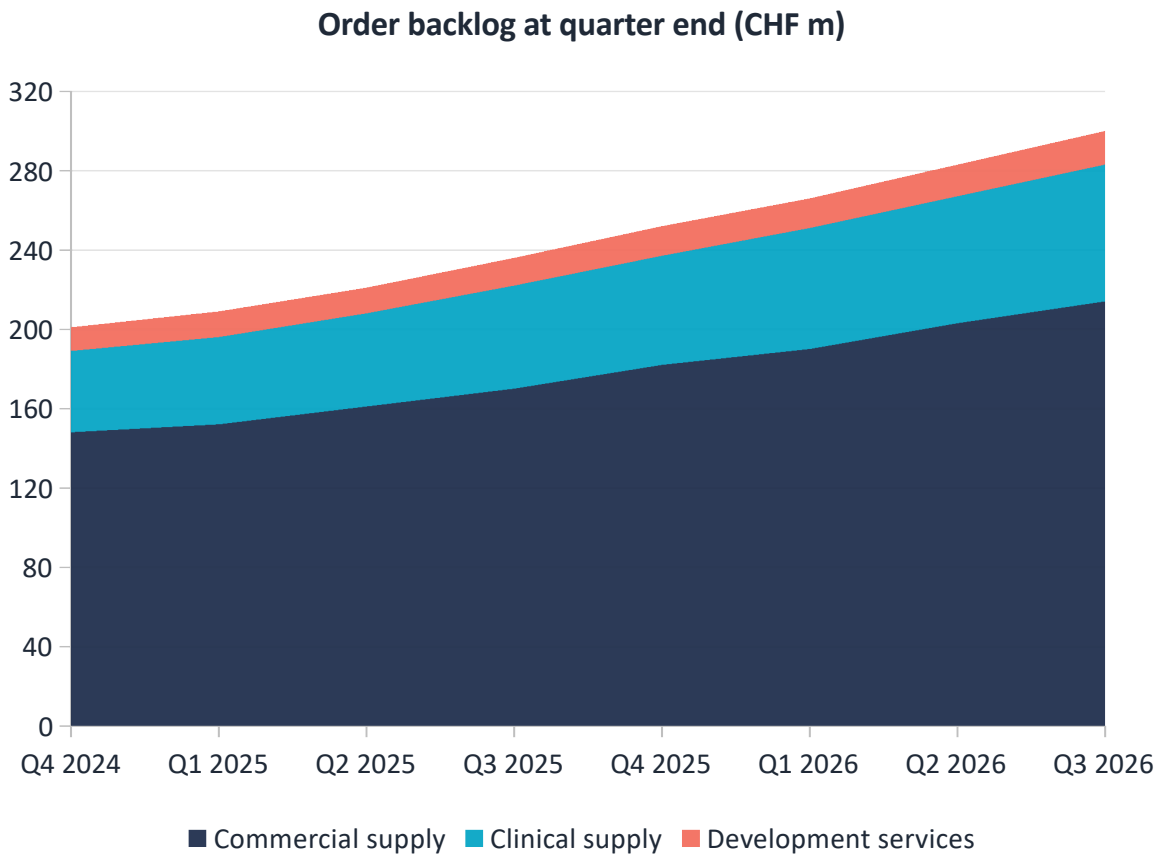


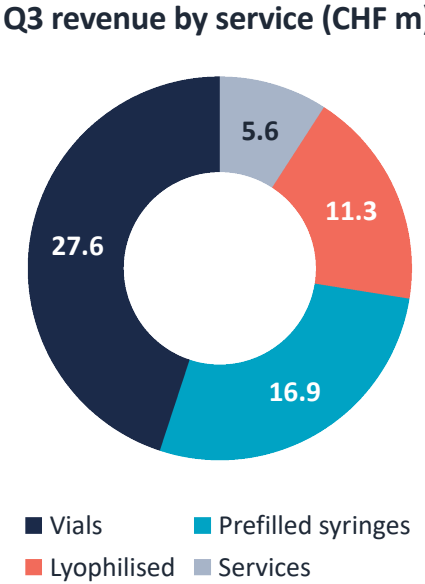

CHF 300 m

backlog at 30 September, 4.9 quarters of revenue; 71 % commercial supply with contracts beyond 2028.

Net cash bridge Q3 2026

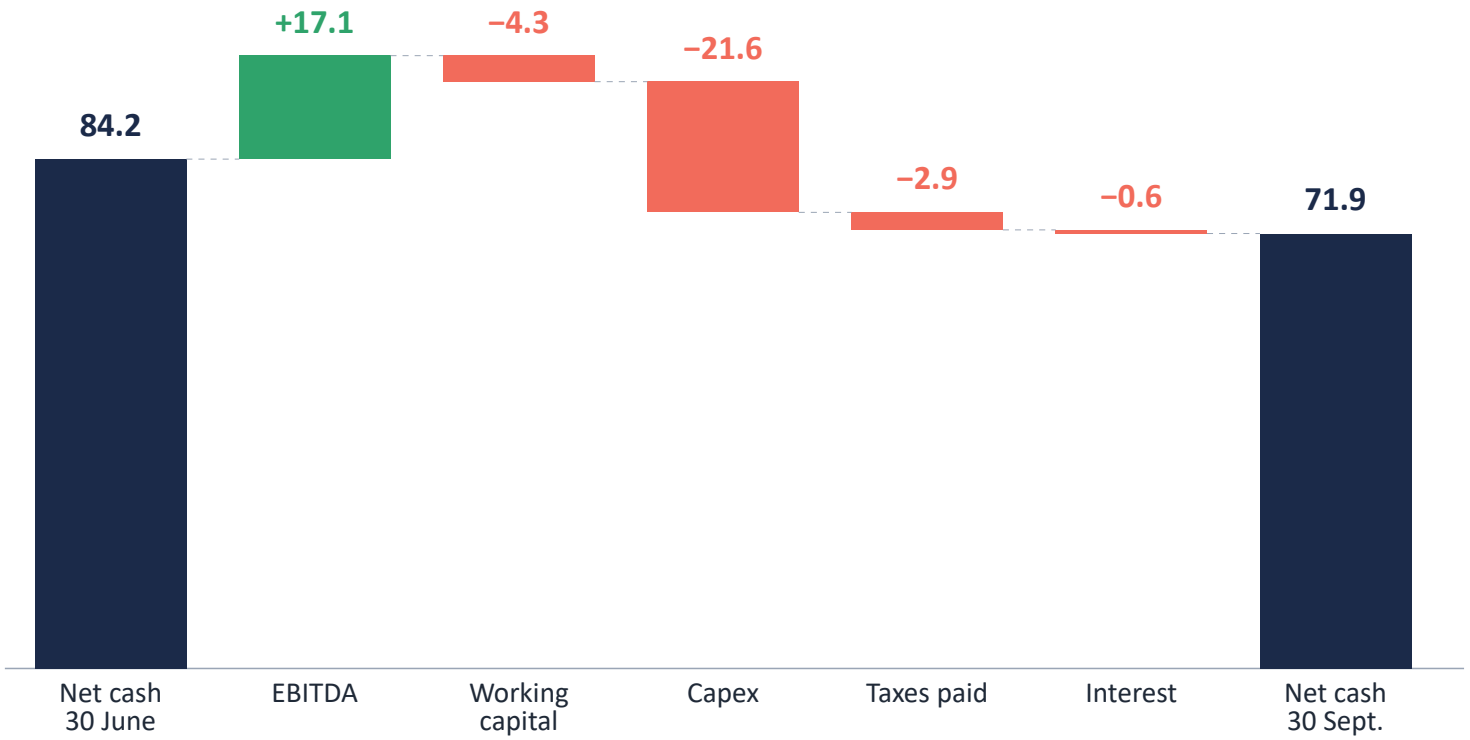

Capex CHF 21.6 m

FL-5 expansion 14.2

LY-4 upgrades 3.1

Maintenance and IT 4.3

Working capital −4.3

Inventory build for the Q4 PFS campaigns (+6.1), partly offset by receivables (−1.8).

Liquidity

Undrawn credit facility CHF 80 m; extension to CHF 120 m proposed for decision.


CORVANE BIOLOGICS


02

Operations and quality

212 batches released, OEE up on both filling lines, CAPA backlog down by 16.

Operations: batches and equipment effectiveness

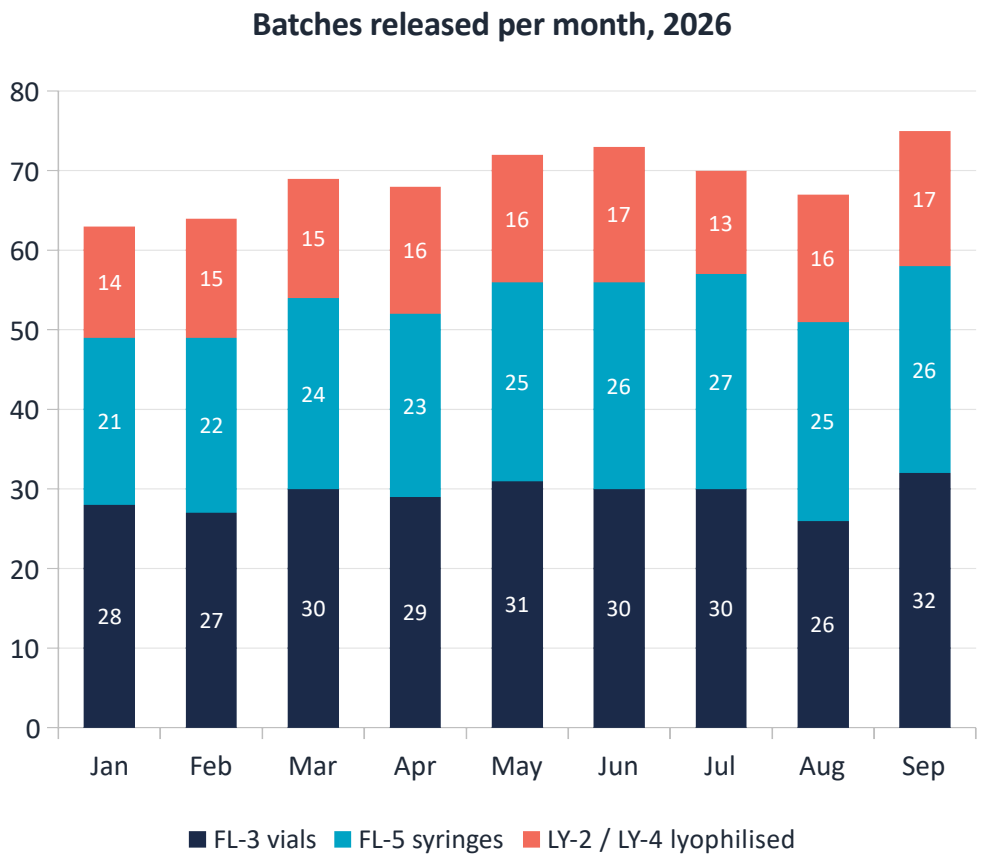

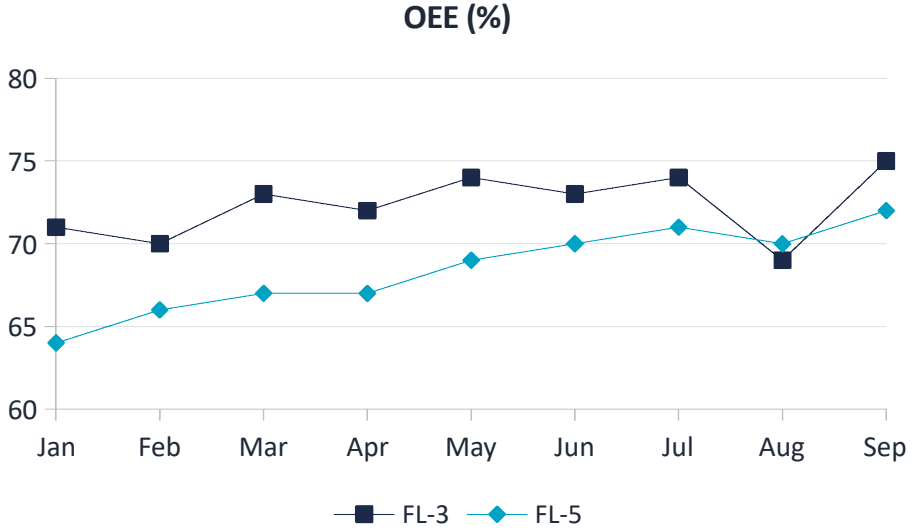

Q3: 212 batches

July: LY-2 condenser repair, 11 days, 9 batches moved to LY-4 in Q4.
August: planned shutdown week on FL-3 (HVAC re-qualification).
FL-5 reached 72 % OEE in September, the target for year-end.

Quality: CAPA status and deviations


CAPA category	Open 1 Jul	New	Closed	Open 30 Sep	Overdue	Status
Deviation-related	46	31	38	39	3	On track
Customer audit findings	18	9	14	13	1	On track
Authority inspection findings	6	0	4	2	0	Closing
Complaints	7	5	6	6	0	On track
Change-control actions	12	8	7	13	2	Watch
Total	**89**	**53**	**69**	**73**	**6**	

Highlights

Right-first-time 97.6 % (target 98.0 %): 5 of 212 batches needed additional review, 3 of them on FL-3 after the stopper supplier change. CAPA 26-118 adds an incoming siliconisation check; effectiveness review in November.

Customer audits: 4 in Q3, no critical findings; the authority follow-up inspection of June is closed except for two documentation actions due 15 November.


Media fills: 6 of 6 passed (FL-3: 2, FL-5: 3, LY-4 transfer: 1).

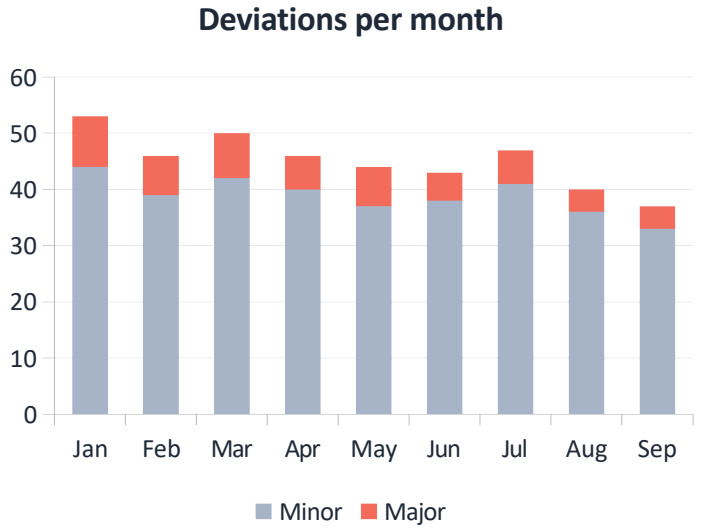

6 overdue CAPA

all with approved extensions; the oldest is 41 days late (change control CC-26-044, supplier qualification).


Risk heat map and top risks

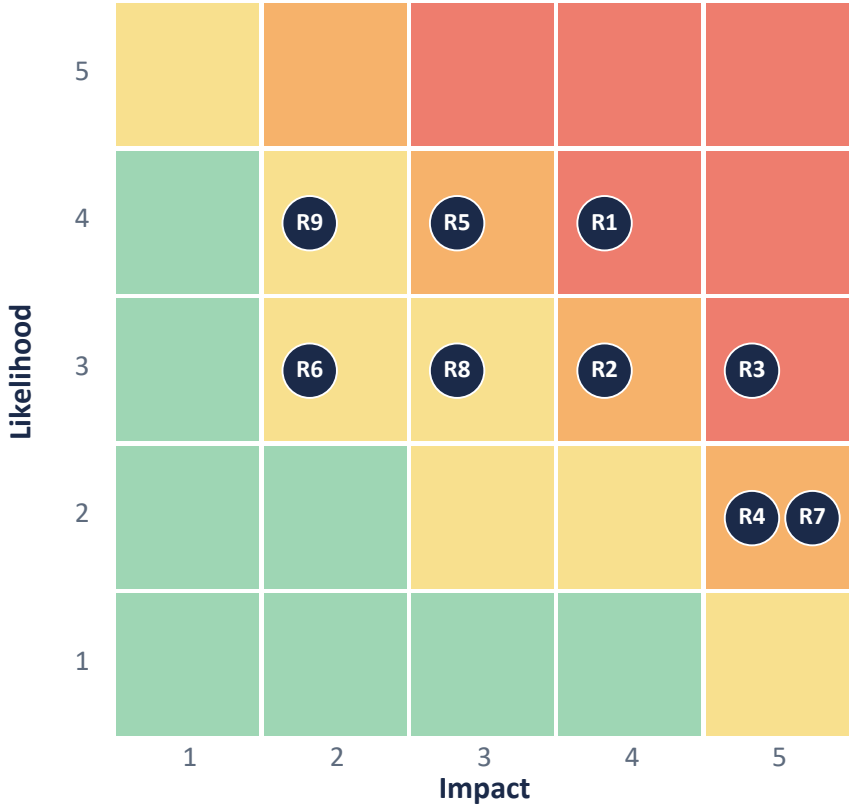

ID	Risk	Owner	Score	Trend
R1	Single-source vial glass supply	Supply chain	16	→
R3	Customer concentration (top 3: 46 %)	CBO	15	→
R2	Lyophilisation capacity until LY-5	COO	12	↑
R5	Operator turnover on FL-5	CHRO	12	↑
R4	Annex 1 contamination control gaps	CQO	10	↓
R7	Cyber attack on MES / OT	CFO	10	→
R8	FL-5 expansion delay	COO	9	→
R9	CHF strength vs EUR and USD	CFO	8	→
R6	Energy prices	CFO	6	↓

Score = likelihood × impact (1–5 each). Trend against the July review. R2 rises until LY-5 is approved; R4 falls after the contamination control strategy update of August.

Project portfolio: value, probability and capital

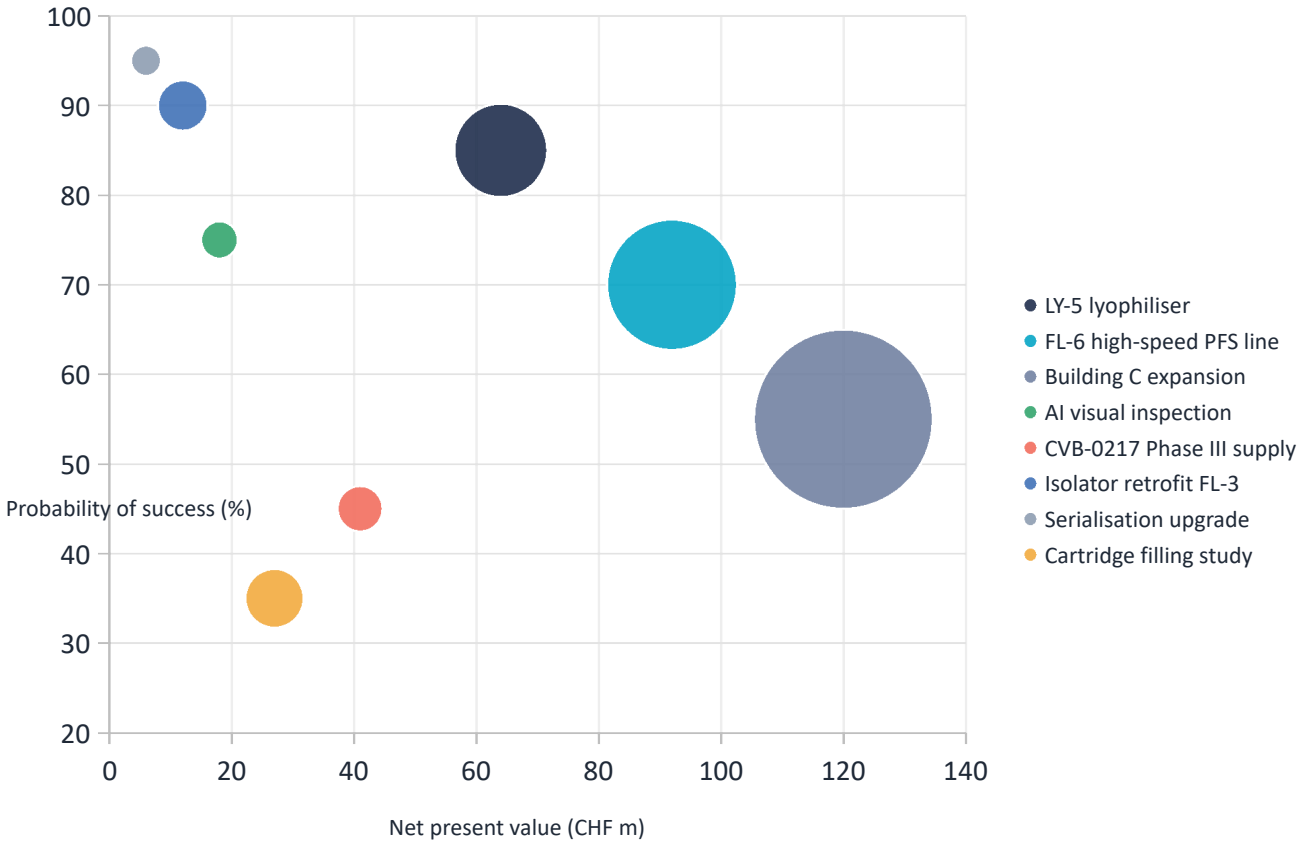

Bubble size = capex

Eight projects, CHF 297 m capex in total, CHF 380 m risk-adjusted NPV.

For decision today

LY-5 lyophiliser: CHF 38 m, NPV CHF 64 m, payback 5.2 years; removes risk R2 from 2028.

Next board

FL-6 business case with two anchor customers; Building C only after FL-6.

Major projects: status

Project	Sponsor	Budget (CHF m)	Spent	Schedule	Cost	Scope	Next milestone
FL-5 capacity expansion	COO	48.0	36.1	G	A	G	IQ/OQ start, 18 Nov.
LY-4 condenser and CIP upgrade	COO	7.5	6.2	A	G	G	Requalification, Dec.
MES release 4 (electronic batch record)	CFO	5.8	3.0	A	A	G	Go-live FL-3, Jan. 2027
Contamination control strategy update	CQO	1.2	0.9	G	G	G	Annex 1 gap closure, Nov.
CVB-0217 Phase III readiness	CBO	9.0	2.4	G	G	A	Engineering run 2, Feb. 2027
Warehouse automation, Building B	COO	6.4	1.1	R	G	G	Vendor award, Nov.

G on track A at risk, mitigation in place R off track, board attention

Warehouse automation is off track: the preferred vendor withdrew in September. Re-tender launched; award in November, completion moves from Q2 to Q4 2027 without budget change. Interim: second shift in manual picking.

FL-5 expansion: cost at risk by CHF 1.4 m (isolator glove-port retrofit); covered by the project contingency of CHF 3.0 m.

FL-5 expansion: progress by workstream



FL-5 isolator, second filling module during installation, September 2026


Key dates

18 November: IQ/OQ start

February 2027: three media fills

April 2027: first commercial batch

Capacity after expansion: 52 million syringes a year (+65 %).

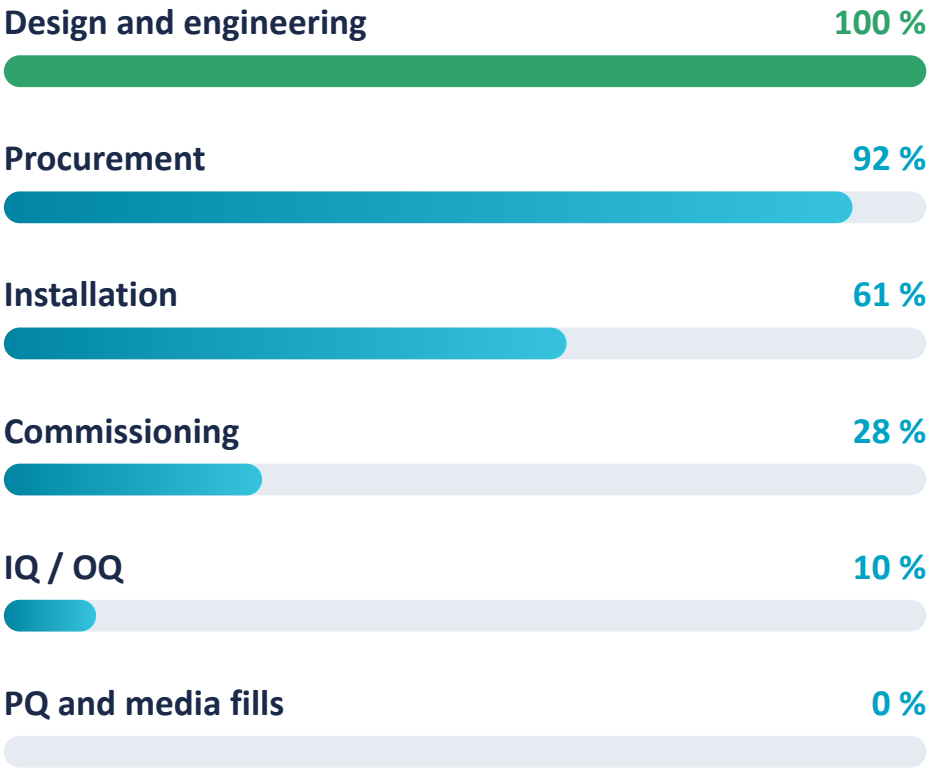

CORVANE BIOLOGICS

03

Outlook and decisions

FY 2026 guidance raised; two decisions requested from the Board.

FY 2026 outlook and decisions requested

FY 2026	Previous guidance	New guidance	Budget
Revenue (CHF m)	232 – 238	**238 – 242**	231.0
EBITDA margin	26 – 27 %	**27 – 28 %**	26.0 %
Capex (CHF m)	68	**64**	70
Batches released	830+	**850+**	820

Assumptions

- Q4 PFS campaigns confirmed by purchase orders (CHF 19.4 m)
- LY-2 back to full capacity from 1 November
- EUR/CHF 0.93 and USD/CHF 0.84 for the rest of the year
- No impact from the FL-5 qualification on existing FL-5 output
  - IQ/OQ runs on the second module only

DECISION 1

Approve the LY-5 lyophiliser investment of CHF 38.0 m (capex 2027–2028).

DECISION 2

Approve the extension of the revolving credit facility from CHF 80 m to CHF 120 m, maturity 2031.

FOR INFORMATION

Q3 quality report and CAPA plan; 2027 budget meeting on 10 December 2026.

Appendix A: income statement by quarter

CHF million	Q1 2026	Q2 2026	Q3 2026	YTD 2026	YTD budget	FY 2025
Revenue	**56.2**	**58.7**	**61.4**	**176.3**	**172.5**	**212.5**
Cost of goods sold (excl. D&A)	−33.8	−35.0	−36.2	−105.0	−103.8	−129.0
Gross profit	**22.4**	**23.7**	**25.2**	**71.3**	**68.7**	**83.5**
Selling, general and administrative	−5.9	−6.0	−6.1	−18.0	−18.6	−23.2
Process development	−1.9	−1.9	−2.0	−5.8	−6.2	−7.6
EBITDA	**14.6**	**15.8**	**17.1**	**47.5**	**43.9**	**52.7**
EBITDA margin	26.0 %	26.9 %	27.8 %	26.9 %	25.4 %	24.8 %
Depreciation and amortisation	−5.7	−5.8	−5.9	−17.4	−18.0	−20.6
EBIT	**8.9**	**10.0**	**11.2**	**30.1**	**25.9**	**32.1**
Net financial result	−0.7	−0.6	−0.6	−1.9	−2.1	−2.9
Income taxes	−1.2	−1.4	−1.6	−4.2	−3.6	−4.4
Net profit	**7.0**	**8.0**	**9.0**	**24.0**	**20.2**	**24.8**

Appendix B: KPI definitions

KPI	Definition	Target 2026
Right first time	Batches released without deviation or additional review, divided by all batches released	≥ 98.0 %
On time in full	Batches shipped on the confirmed date and in the confirmed quantity, divided by all batches shipped	≥ 95.0 %
OEE	Availability × performance × quality, filling lines only, planned production time as base	FL-3 ≥ 74 %, FL-5 ≥ 72 %
Lost-time injury rate	Injuries with at least one lost working day per 200,000 hours worked, employees and contractors	< 0.5
Order backlog	Value of firm purchase orders and binding forecasts not yet invoiced, at quarter end	–
Net cash	Cash and cash equivalents minus financial debt (excluding leases)	–
Overdue CAPA	Corrective or preventive actions past their approved due date, extensions included	≤ 5
